

Date: Wednesday, 5/2/2007 3:47:54 PM
 User: Kim Johnston

Process Sheet

Customer	: CU-DAR001 Dart Helicopters Services	Drawing Name	: 212/205 HIGH AFT X-TUBE ASSEMBLY
Job Number	: 32147		
Estimate Number	: 10257		
P.O. Number	: <i>N/A</i>	Part Number	: D212664201
This Issue	: 5/2/2007	S.O. No.	: <i>N/A</i>
Prsht Rev.	: NC	Drawing Number	: D212-664-241 REV C
First Issue	: <i>N/A</i>	Project Number	: N/A
Previous Run	: 32146	Drawing Revision	: C
		Material	: <i>N/A</i>
		Due Date	: 5/30/2007
Written By	: <i>[Signature]</i>	Qty:	1 Um: Each
Checked & Approved By	: <i>[Signature]</i>		
Comment	Est Rev:E 04-02-16 Reformat K/DS Est Rev:F 06-03-29 Remove Comments on Pick List JLM Est Rev:G 07-04-30 As per Rev C JLM		

Additional Product

Job Number:



Seq. #:	Machine Or Operation:	Description:
---------	-----------------------	--------------

1.0	DC	DOCUMENT CONTROL
-----	----	------------------



Comment: DOCUMENT CONTROL

Photocopy bluefile and create labels as per PPP D212-664-201CHG003

KS 07-05-18 *2F 07/05/05*

2.0	D6006129	Crosstube material
-----	----------	--------------------



Comment: Qty.: 1.0000 Each(s)/Unit Total: 1.0000 Each(s)

Pick:

Qty Part number Description Batch

1 D6006-129 Crosstube *B2911R*

Check OD = 3.250"; ID = 2.220"

2F 07/05/05

3.0	MORI SEIKI	MORI SEIKI CNC LATHE LARGE
-----	------------	----------------------------



Comment: MORI SEIKI CNC LATHE LARGE

1-Fill tube with sand & install plugs DT8534 on both ends as per Folio FA114

2-Turn first side as per Folio FA114

3-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D212-664-241.

2F 07/05/05

4.0	QC1	INSPECT ALL DIM TO DIM SHEET
-----	-----	------------------------------



Comment: INSPECT ALL DIM TO DIM SHEET

2F 07/05/05

Dart Aerospace Ltd

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes ☒ No ☐ DQA: DD Date: 07/08/01
 QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			
070510	7.0	2 cuffs found to be long by 0.38" above the max tolerance. Operator error caught during auditing.	<i>[Signature]</i> 051042	Cuffs acceptable. Remaining dimensions are good.	<i>[Signature]</i> 070510	<i>[Signature]</i> 070510	<i>[Signature]</i> 051042	<i>[Signature]</i> 070510

NOTE: Date & initial all entries

Date: Wednesday, 5/2/2007 3:47:54 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 212/205 HIGH AFT X-TUBE ASSEMBLY

Job Number: 32147

Part Number: D212664201

Job Number:



Seq. #:

Machine Or Operation:

Description :

12.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

DP 7-5-22

13.0

BENDING

BENDING MACHINE



Comment: BENDING MACHINE

Bend tube as per Dwg D212-664-241 using CNC bender program 212-af and Folio FT007

EL 7-5-28

14.0

QC15

DIMENSIONAL CHECK OF X-TUBES



Comment: DIMENSIONAL CHECK OF X-TUBES

20706-01 (U)

15.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Drill pilot holes in tube as per Dwg D212-664-241 using drill Jig DT8550 & DT8551

2-Ream hole to finish size in tube as per Dwg D212-664-241 using drill Jig DT8550 & DT8551. Check dimensions between holes, both sides on both cuffs, to ensure alignment with saddle holes.

3-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D212-664-241

7-6-18
EL 7-6-19

16.0

HAND FINISHING1

HAND FINISHING RESOURCE #1



Comment: HAND FINISHING RESOURCE #1

Chemical Conversion Coat as per QSI 005 4.1 within 24 hours of bending and drilling

JD 7-6-19

17.0

QC3

INSPECT POWDER COAT/CHEMICAL CONVERSION



Comment: INSPECT POWDER COAT/CHEMICAL CONVERSION

20706-20 (U)

18.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

20706-20 (U)

19.0

OUTSIDE SERV.10

OUTSIDE SERVICES -LG



Comment: Sub-Contracting OUTSIDE SERVICES

Liquid Penetrant Inspection as per QSI 038

Issue P/O: 4012

20706/06/21 (U)

LPI as per ASTM 1417 Level 2

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Wednesday, 5/2/2007 3:47:54 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 212/205 HIGH AFT X-TUBE ASSEMBLY

Job Number: 32147

Part Number: D212664201

Job Number:



Seq. #:

Machine Or Operation:

Description :

Attach copy of NDT results to work order

20.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Inspect for transit damage Ensure copy of NDT results attached to work order.

CP 07/06/26 (1)

21.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: DIMENSIONAL CHECK

Inspect for damage & ensure results are as per Dwg D212-664-241

CP 07/06/27 (1)

22.0

SPRAY PAINTING

SPRAY PAINTING



Comment: SPRAY PAINTING

1-Prime inside and outside crosstube as per QSI 005 4.2

2-Paint outside crosstube with White Imron as per QSI 005 4.2

*} RT 07-07-20
RT 07-07-25*

23.0

QC14

INSPECT SPRAY PAINT



Comment: Inspect Spray Paint

Then, Wrap in plastic bag to protect from scratches

ml 010121

(1)

24.0

D29401

Support



Comment: Qty.: 2.0000 Each(s)/Unit Total : 2.0000 Each(s)

Pick:

Qty Part number Description Batch

2 D2940-1 Support

25544 ml 010121

25.0

D3595

Rubber Cushion (per sq ft)



Comment: Qty.: 0.0242 sf(s)/Unit Total : 0.0242 sf(s)

Rubber Cushion (per sq ft)

.63" x 5.300

Batch:

33542 ml 010123

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Wednesday, 5/2/2007 3:47:54 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 212/205 HIGH AFT X-TUBE ASSEMBLY

Job Number: 32147

Part Number: D212664201

Job Number:



Seq. #:

Machine Or Operation:

Description :

26.0

MS2192028

Clamp(per MIL-DTL-8783C)



Comment: Qty.: 4.0000 Each(s)/Unit Total : 4.0000 Each(s)

Pick:

Qty Part number Description Batch

4 MS21920-28

Clamp

103896 ml 010121

27.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Install supports with magnobond as per QSI 015 Adhere for for 12 Hrs

A/R 6398 Magnobond

Batch: 104723

Expiry Date: 04/2008

Time: 5:00 pm

ml 010121

2-Install clamps as per Dwg D212-664-241. Torque clamps to 80-100 in lb.

28.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

En 07/07/31 (41)

29.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Pick Packing Kit

30.0

D34281

Placard



Comment: Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)

Placard

Batch:

B26295

31.0

AN640A

Bolt



Comment: Qty.: 4.0000 Each(s)/Unit Total : 4.0000 Each(s)

Bolt

Batch:

M103172

3X

M104374

1X - Cu

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes ☒ No ☐ DQA: ☒ Date: 07/08/01
 QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Wednesday, 5/2/2007 3:47:55 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 212/205 HIGH AFT X-TUBE ASSEMBLY

Job Number: 32147

Part Number: D212664201

Job Number:



Seq. #:

Machine Or Operation:

Description :

32.0

AN641A

Bolt



Comment: Qty.: 2.0000 Each(s)/Unit Total : 2.0000 Each(s)

Bolt

Batch: M100743

33.0

AN960JD616

Washer



Comment: Qty.: 18.0000 Each(s)/Unit Total : 18.0000 Each(s)

Washer

Batch: M103641

34.0

MS21042L6

Nut



Comment: Qty.: 6.0000 Each(s)/Unit Total : 6.0000 Each(s)

Nut

Batch: M101660

35.0

QC4

INSPECT 100% KITS FOR COMPLETENESS



Comment: INSPECT 100% KITS FOR COMPLETENESS

36.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: HAND FINISHING RESOURCE #1

Identify and pack for shipping as per PPP D212-664-201

37.0

QC21

FINAL INSPECTION/W/O RELEASE



Comment: FINAL INSPECTION/W/O RELEASE

Job Completion



Jul 07 07:31

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART AEROSPACE LTD		Work Order: 32147
Description: Crosstube Assembly (205/212 High Aft)		Part Number: D212-664-241
Inspection Dwg: D212-664-241 Rev: B C PH 07-05-02		Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST

☒ First Article ☐ Prototype

Inspection Sheet Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
SIDE A	0.200	+/-0.010	.200	/		
	R0.063	+/-0.010	.063	/		
	2.990	+0.005/-0.000	2.994	/		
	5.237	+/-0.030	5.237	✓	✓	5.305
	2.600	+0.005/-0.000	2.604	/		
	2.686	+0.005/-0.000	2.690	/		
	2.770	+0.005/-0.000	2.774	/		
	2.854	+0.005/-0.000	2.858	/		
	2.938	+0.005/-0.000	2.942	/		
	3.021	+0.005/-0.000	3.025	/		
	3.133	+0.005/-0.000	3.137	/		
	3.179	+0.005/-0.000	3.183	/		
SIDE B	0.200	+/-0.010	.200	/		
	R0.063	+/-0.010	.063	/		
	2.990	+0.005/-0.000	2.994	/		
	5.237	+/-0.030	5.237	✓	✓	5.305
	2.600	+0.005/-0.000	2.604	/		
	2.686	+0.005/-0.000	2.690	/		
	2.770	+0.005/-0.000	2.774	/		
	2.854	+0.005/-0.000	2.858	/		
	2.938	+0.005/-0.000	2.942	/		
	3.021	+0.005/-0.000	3.025	/		
	3.133	+0.005/-0.000	3.137	/		
	3.179	+0.005/-0.000	3.183	/		
	124.36	+/-0.020	124.36	/		

Measured by: J.F.	Audited by: SA	Prototype Approval:	N/A
Date: 07/05/10	Date: 07.05.10	Date:	N/A

Rev	Date	Change	Revised by	Approved
A	05.04.27	New Issue (P/O D412-664-201)	KJ/JLM	
B	06.03.09	Tolerance for 5.237 was +/-0.001	KJ/JLM	


DART AEROSPACE LTD		Work Order:	32147
Description: Crosstube High Aft (205/212)		Part Number:	D212-664-201
Inspection Dwg: D212-664-241		Rev: B C PH 07.05.02	Page 1 of 1

Required Dimension	Min	Max
Height	24.17 24.24	24.38 24.43
1/2 Span	53.59 53.66	53.78 53.85
Angle	49	52
Total Span	107.32	107.56

107.13

107.70

PH 07.05.02

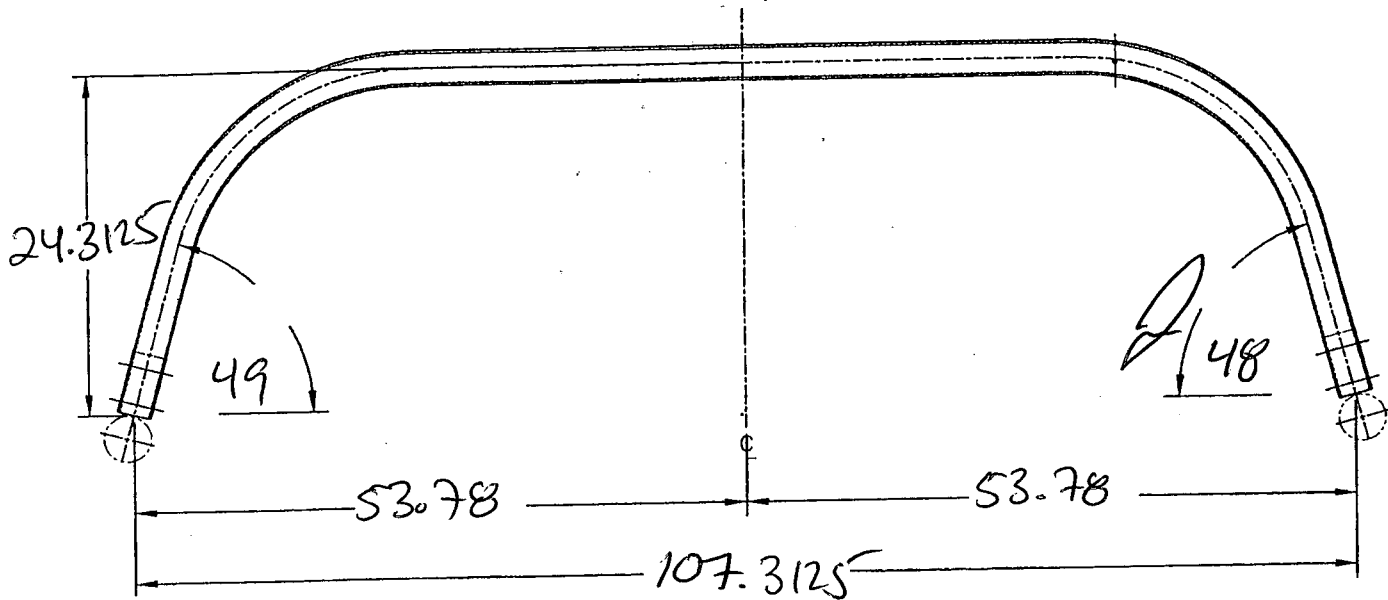

Comments

QC15 Inspection	Date 07.06.04
Date	

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	



DESIGN PH	DRAWN BY PH	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED J	APPROVED [Signature]	DRAWING NO. D212-664-241	REV. C SHEET 1 OF 3
DATE 07.03.08		TITLE CROSSTUBE ASS'Y (205/212 HI AFT) NTS	
A	00.12.12	NEW ISSUE	
B	05.02.04	ADD HOLES FOR COMPATABILITY WITH BHT/AA SKIDTUBES	
C	07.03.08	REMOVE -1009 ABRASION STRIP; ADD MAGNOBOND 6398, CUSHION, REVERSE CLAMPS	

RELEASED
07.04.24
PER E.A.N. 0289

Qty	Part Number	Description
X	D212-664-241	CROSSTUBE ASSEMBLY (205/212 HIGH AFT)
1	D6006-129	CROSSTUBE
2	D2940-1	SUPPORT
4	D3595-063-530	RUBBER CUSHION
4	MS21920-28	CLAMP (OR MS21920-30)
A/R	MAGNOBOND 6398	ROCKWELL SPECIFICATION RBO-120-023 ADHESIVE (TEXTRON/BELL SPEC. 299-947-100, TYPE II, CLASS 2 ADHESIVE)






GENERAL NOTES:

- 1) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 2) MATERIAL: MANUFACTURED FROM D6006-129
FINISHED LENGTH = 124.36 ± 0.020
- 3) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 4) PART IS SYMMETRIC ABOUT CENTERLINE
- 5) RUN-OFF PART. BLEND OUT EDGE LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH.
- 6) BEND PROGRESSIVELY WITH A MINIMUM OF 5 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 7) LIQUID PENETRANT INSPECT OUTSIDE SURFACE OF CROSSTUBE PER QSI 038.
- 8) SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS.
- 9) INSTALL D2940-1 SUPPORT USING 0.03" TO 0.06" THICK LAYER OF MAGNOBOND 6398 PER QSI 015. LET CURE FOR 12 HOURS AFTER INSTALLATION AND PRIOR TO PACKAGING.
- 10) INSTALL MS21920-28 CLAMPS WITH D3595-063-530 RUBBER CUSHIONS TO SECURE D2940-1 SUPPORT ON TOP SIDE OF CROSSTUBE. ENSURE CLAMPS ARE OPPOSITE OF CROSSTUBE SUPPORT
NOTE: MS21920-30 CLAMPS CAN BE USED TO ACCOMMODATE VARYING DIAMETERS. ENSURE THERE IS A MINIMUM OF 1.5 THREADS IN SAFETY ON THE NUTS.
- 11) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.
- 12) TORQUE CLAMPS 80 TO 100 IN-LB.

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 32147

Copyright © 2000 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

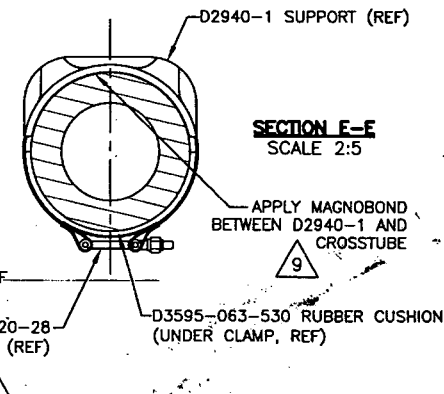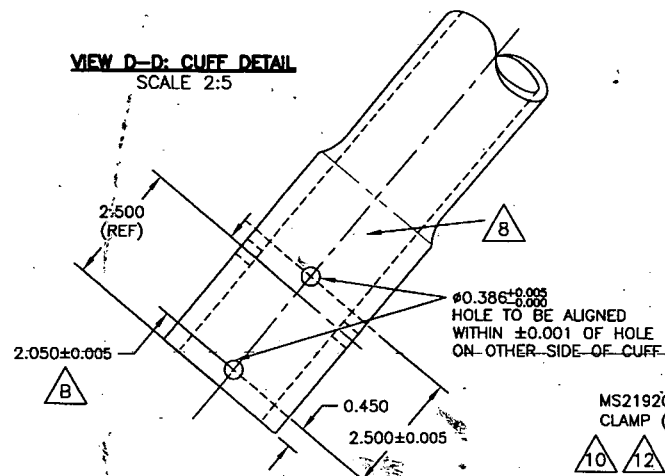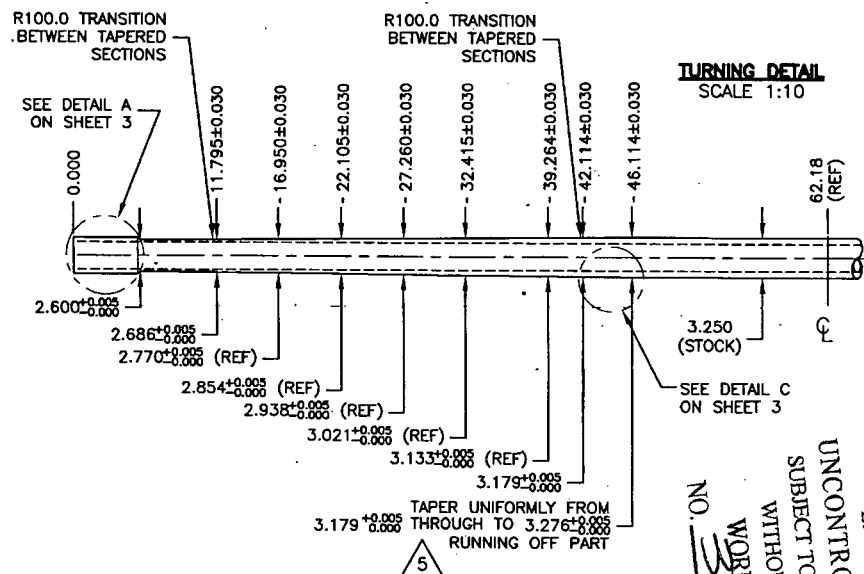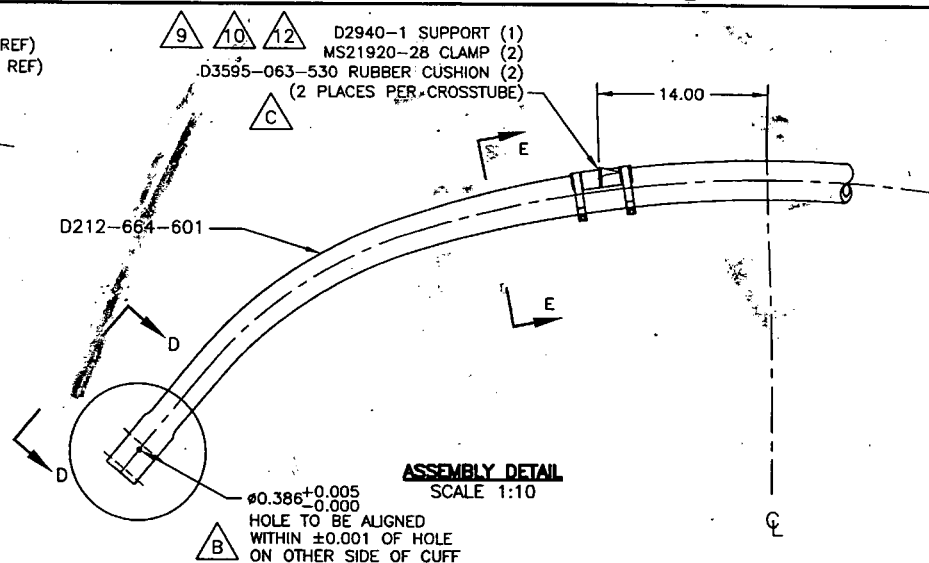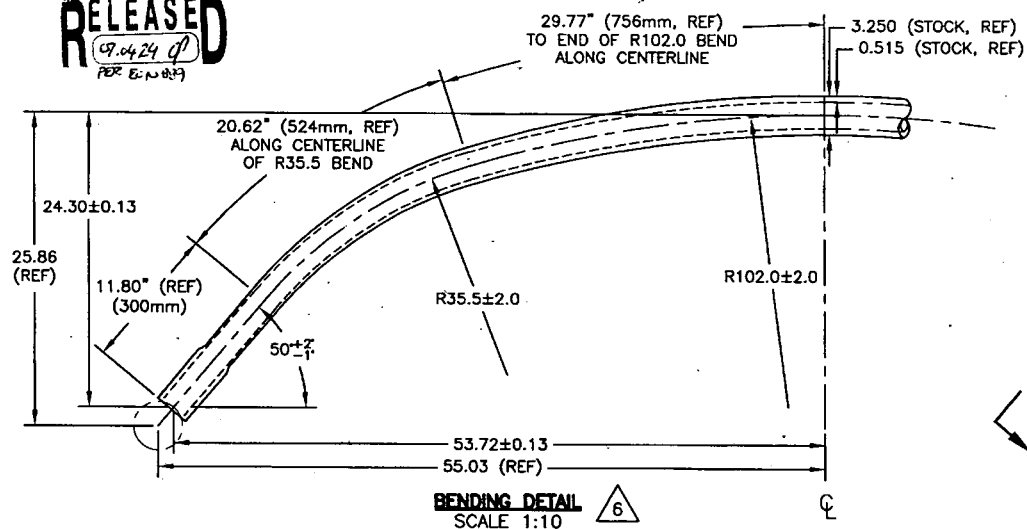


SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 201147


COPYRIGHT © 2000 BY DART AEROSPACE LTD. THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART-AEROSPACE LTD.	DESIGN	DRAWN BY	DART	DART AEROSPACE LTD. HAMMERSLEY, CHICAGO, CANADA
	CHECKED	APPROVED	DRAWING NO.	REV. C
	DATE		D212-664-241	SHEET 2 OF 3
	07.03.08		TITLE	SCALE
			CROSSTUBE ASS'Y (205/212 HI AFT)	1:10

RELEASED
07.04.24
PER ECN 889


DETAIL A: CROSSTUBE CUFF

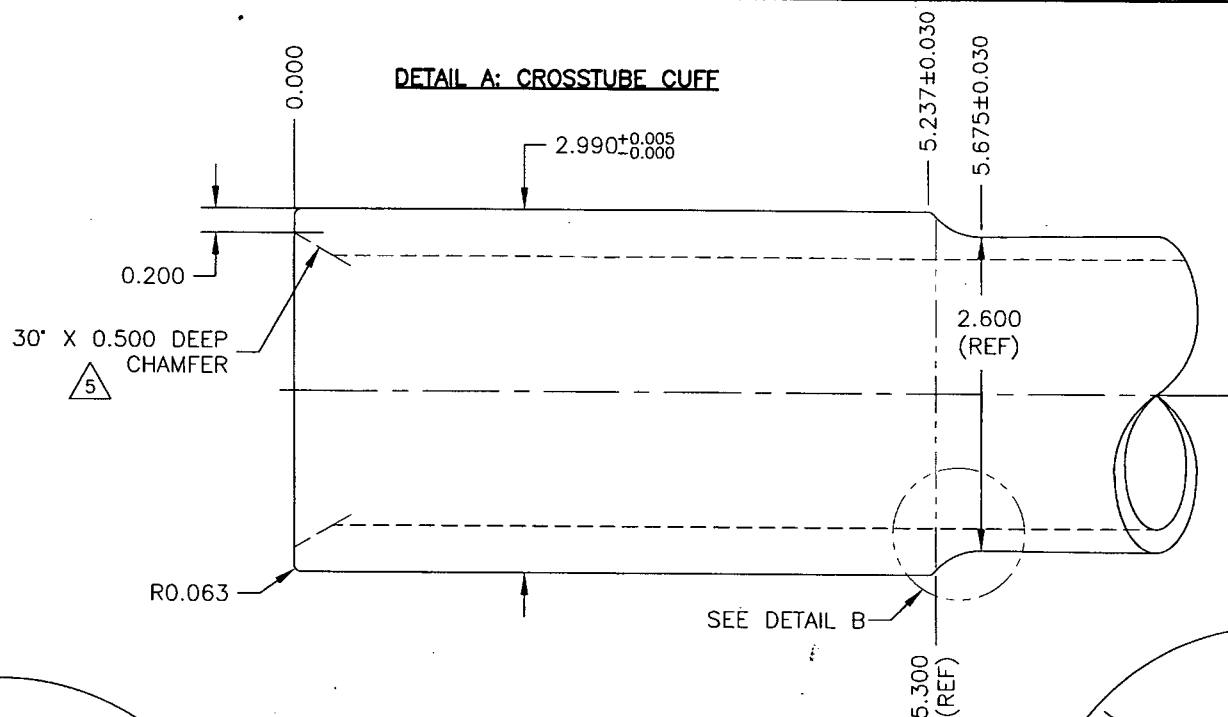

**DETAIL B: CUFF
TRANSITION**
SCALE 4:1

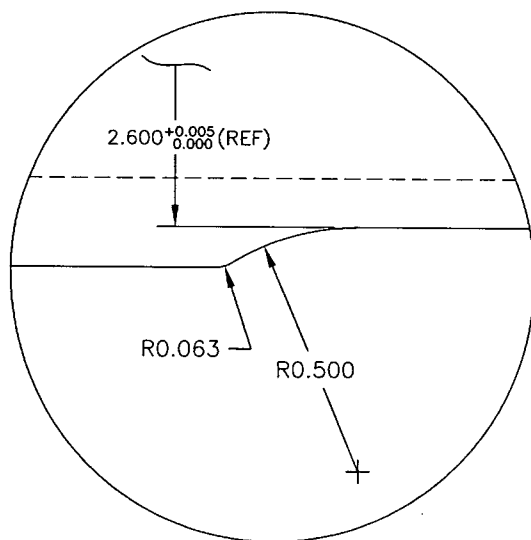


**DETAIL C:
TAPER RUN-OFF**
NOT TO SCALE

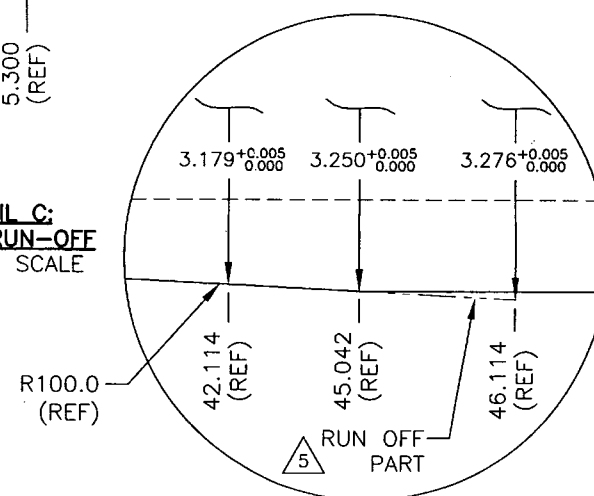

NO. 32147
WORK ORDER
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
SHOP COPY
RETURN TO
ENGINEERING

COPYRIGHT © 2000 BY DART AEROSPACE LTD.		DESIGN	DRAWN BY	DART	DART AEROSPACE LTD.
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		CHECKED	APPROVED	DRAWING NO.	REV. C
		DATE		D212-664-241	SHEET 3 OF 3
		07.03.08		TITLE	SCALE
				CROSSTUBE ASS'Y (205/212 HI AFT)	1:1



HeathAir

INTERNATIONAL (1991) INC.

681 Ave. Lepine, Dorval, Québec H9P 1G3
Tél.: (514) 636-1000 • Fax: (514) 636-0031

W.O. N° 36755

A.M.O. Number: 46/90

NON-DESTRUCTIVE TESTING REPORT

AIRCRAFT / COMPONENT INFORMATION

REGISTRATION:

MODEL/TYPE:

SERIAL NUMBER:

TOTAL HR/LDG:

OPERATED BY:

BASED AT:

INSPECTION REQUIREMENTS

Carry out FPI of (16) cross tube (external surface) as per ASTM E-1417-05 and the Dart QSI 038, Section 4.1.1 (on file at client) - parts delivered to HeathAir.

Qty (3) P/N D206-667-201 S/N's B30318, B30442 & B30441

Qty (4) P/N D206-667-203BL S/N's B32672, B32458, B32671 & B32457

Qty (1) P/N D407-667-205 S/N B31040

Qty (1) P/N D206-667-201 S/N B30440

Qty (4) P/N D212-664-201 S/N's B32148, B32146, B32149 & B32147

Qty (3) P/N D206-667-103BL S/N's B32667, B32455 & B32456

☐ RADIOGRAPHY

☐ ULTRASONIC

☒ PENETRANT

☐ MAGNETIC PARTICLE

☐ EDDY CURRENT

INSPECTION REPORT

Fluorescent penetrant inspection was performed in accordance with the above requirements on (16) cross tubes.

Note: A Level 3 penetrant was substituted for the requested Level 2 (3 is more sensitive)
Ardrox 970P25E Batch #04B503.

All (16) cross tubes passed inspection.

THE MAINTENANCE DESCRIBED ABOVE HAS BEEN PERFORMED IN ACCORDANCE WITH
THE APPLICABLE STANDARDS OF AIRWORTHINESS

INSPECTED BY:

S. FLECHER

DATE June 22, 2007

INSPECTION
STAMP(S) Not Required

CUSTOMER INFORMATION

CUSTOMER: Dart Aerospace

P.O. NUMBER

4012
Chantel

ADDRESS:

CONTACT NAME:

LABOUR

@

\$

MATERIALS

@

TRAVEL EXPENSES

@

GST

HOTEL EXPENSES

@

PST

INVOICE NO.

TOTAL \$

WHITE COPY - INSPECTION FILE • YELLOW COPY - CUSTOMER • PINK COPY - ACCOUNTANT
